McMurdo Station, Ross Island

BUILDING INFORMATION SHEET

Core Storage

Location ID: B003

Provides refrigerated storage at McMurdo Station and supplements the refrigerated storage capacity of Building 001, CSEC. It currently does not provide freezer space, but an addition planned for construction during the 1999 winter will add the capacity for freezer storage space. Building 003 is an insulated building with a gabled roof located near Building 001. It is composed of three areas, the entryway/foyer, refrigerated room, and attic space with mechanical room.



Photo 1: *Core Storage*

General Structure Information

Usage

Core Storage Facility

Construction Type

The facility is a prefabricated, insulated building with a gable roof. The wall panels are 5-inches thick with foamed-in-place
urethane insulation. Interior and exterior skins are galvanized steel. Panels are secured in place with a camlock device.

Year Constructed

1996

Dimensions

21'2" x 30'9"

Floor Area

Floor	Area
Floor 1	630 sq ft
Total	630 sq ft

HVAC System

Heating

Four electric Chromolax baseboard heaters with fan-forced air and adjustable thermostats. Powered by the baseboard heater contactor and controlled
by Johnson Controls System 350.

Refrigeration

Two air-cooled 3-phase, 208V condensers with Copeland Copelmatic semi-hermatic compressors

Fuel Tank

None

Water and Sewer

Water Service	Not connected
Sewer Service	Not connected

Electrical Service

Service Feeder	Feeder B
Transformer	XF300 B-7
Electrical Service	208/120V, 3PH

Fire System

Fire Panel Type	Fire detection system for Building 003 is wired into the Building 001, KFRTI-WP-8 panel, zone 7, which is located in room 178, Phase I. Building also equipped with pull station and alarm horn.
Heat Detectors	One heat detector is located in the mechanical room. A second heat detector is located in the main, refrigerated room.

Suppression Type	No suppression system.

Floorplans

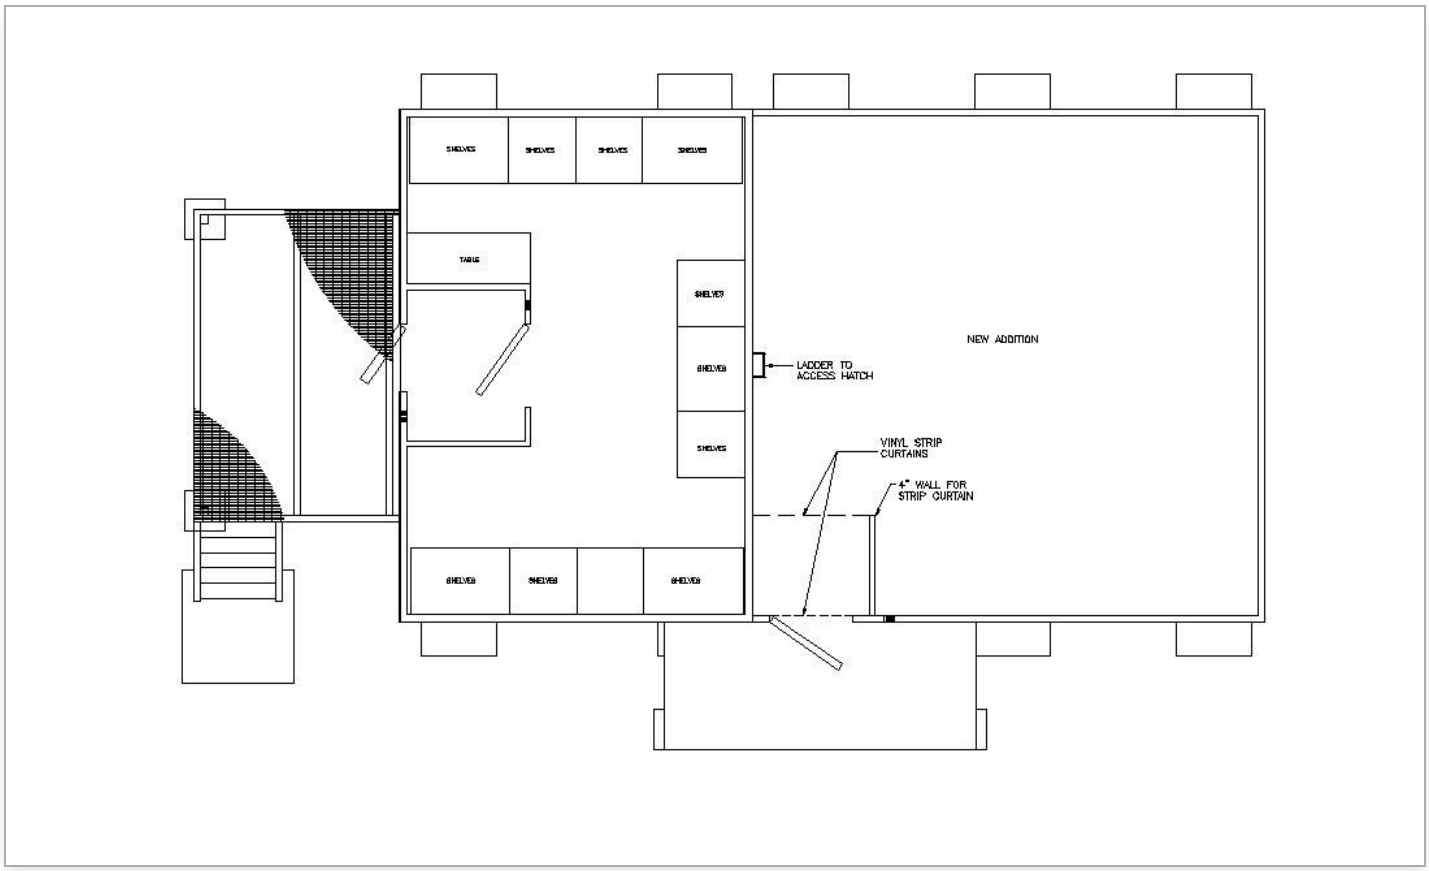


Figure 1: *Core Storage*
