McMurdo Station, Ross Island

BUILDING INFORMATION SHEET

Helo PAX Terminal

Location ID: B036

Passenger waiting and processing area for helicopter flights.

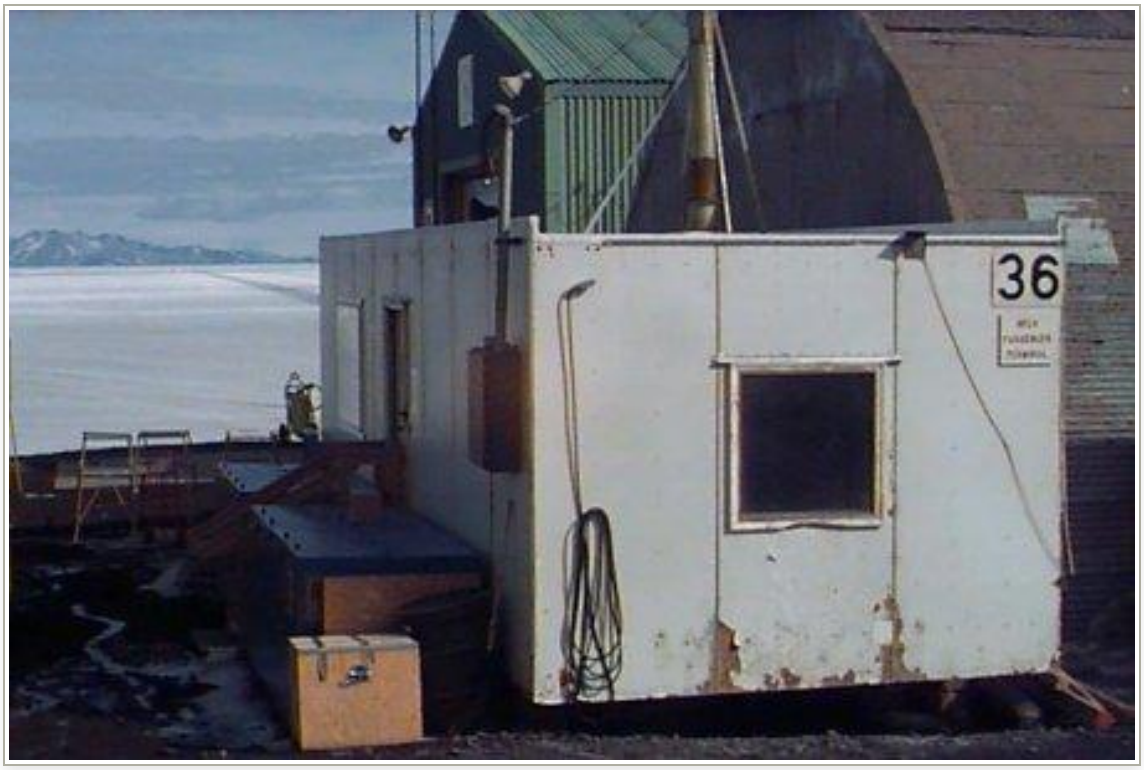


Photo 1: *Helo PAX Terminal*

General Structure Information

Usage	Helicopter Pax Terminal
Construction Type	Wannagan
Year Constructed	N/A

HVAC System

Heating	One Lennox forced air furnace (84,000 Btu/hr output)
Fuel Tank	None

Water and Sewer

Water Service	Not connected
Sewer Service	Not connected
Connections	One Line

Electrical Service

Transformer	XF
Electrical Service	208/120V, 3PH

Fire System

Suppression Type	Automatic dry-chemical fire extinguisher located in furnace room.

Floorplans

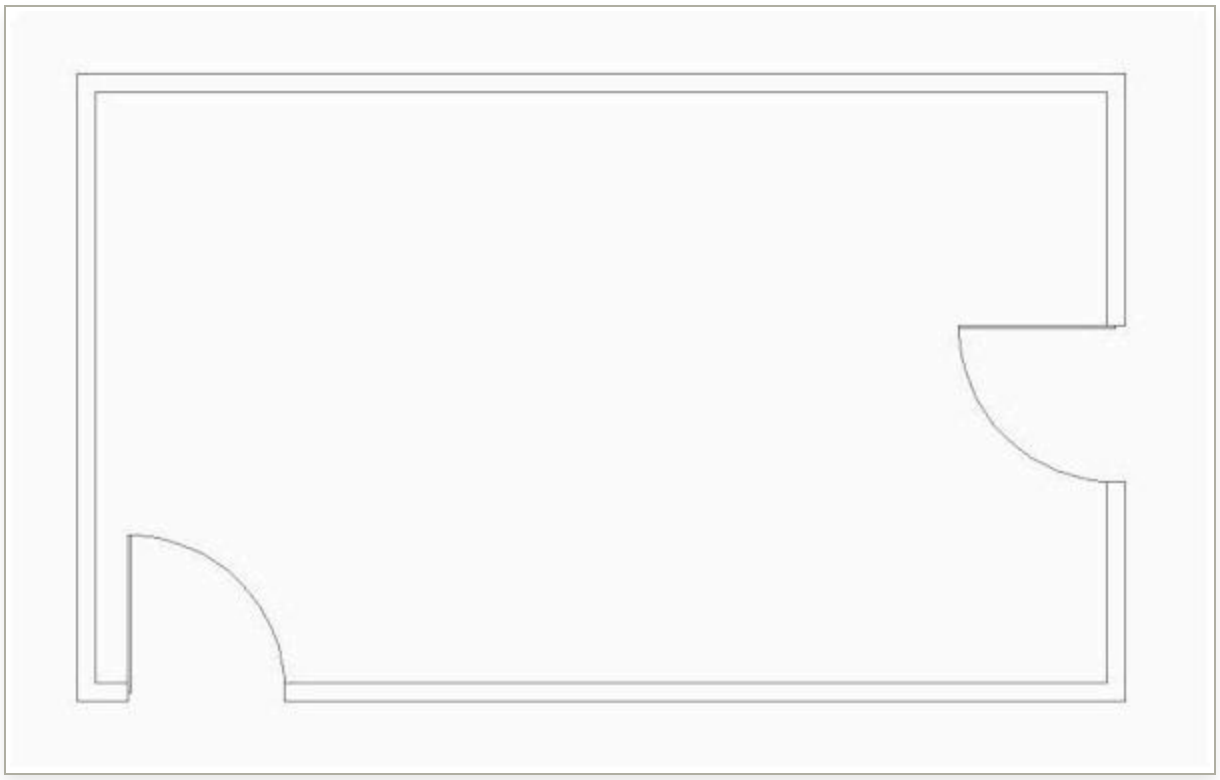


Figure 1: *Helo PAX Terminal*
