McMurdo Station, Ross Island

BUILDING INFORMATION SHEET

Utilities - Facilities

Location ID: B136

Two-story, prefabricated, steel frame structure with insulated metal siding. The interior is a combinations of steel and wood framing with metal and wood panels.



Photo 1: *Utilities - Facilities*

General Structure Information



Automatic External Defibrillator (AED) Locations

This building contains one or more AED devices that may be used in the event of life-threatening cardiac arrhythmia.

- **Mounted near the Work Order and Utility Technicians (UT) offices**

Usage	Facilities Maintenance and Construction Craft Work Center
Occupancy Group	B-2
Maximum Occupancy	60
Construction Type	Type II, 1-Hour, combustible
Year Constructed	1964
Dimensions	60' x 143', 21' x 35' addition

Floor Area

Floor	Area
Floor 1	9,315 sq ft
Floor 2	5,341 sq ft
Total	4,656 sq ft

HVAC System

Heating	One Jackson-Church forced-air, oil-burning unit (500,000 Btu/hr) for the high bay area One Jackson & Churh forced-air, oil-burning unit (500,000 Btu/hr) for the sheet metal shop, PM shop, and upstairs. One Lennox forced-air, oil-burning unit (85,000 Btu/hr) for the lineman shopOne Jackson & Church forced-air, oil-burning unit (200,000 Btu/hr) for the electrical shop
Air Handling Units	None
Fuel Tank	Fuel tank #1: 300 gallons, Fuel tank #2: 800 gallons, Fuel tank #3: 800 gallons

Water and Sewer

Water Service	Not connected
Sewer Service	Not connected
Connections	Sinks: 0 Toilets: 0 Urinals: 0 Showers: 0 Water Cooler: 0
Water Heater	None

Electrical Service

Service Feeder	Feeder D
Electrical Service	208/120V, 3PH - 460V, 3PH

Fire System

Fire Panel Type	King-Fisher KFRTI-20 industrial radio and control system (IRAC) panel, pull stations, and alarm horns.
Heat Detectors	Located throughout building
Suppression Type	Automatic dry-chemical fire extinguisher located over furnaces.

Floorplans

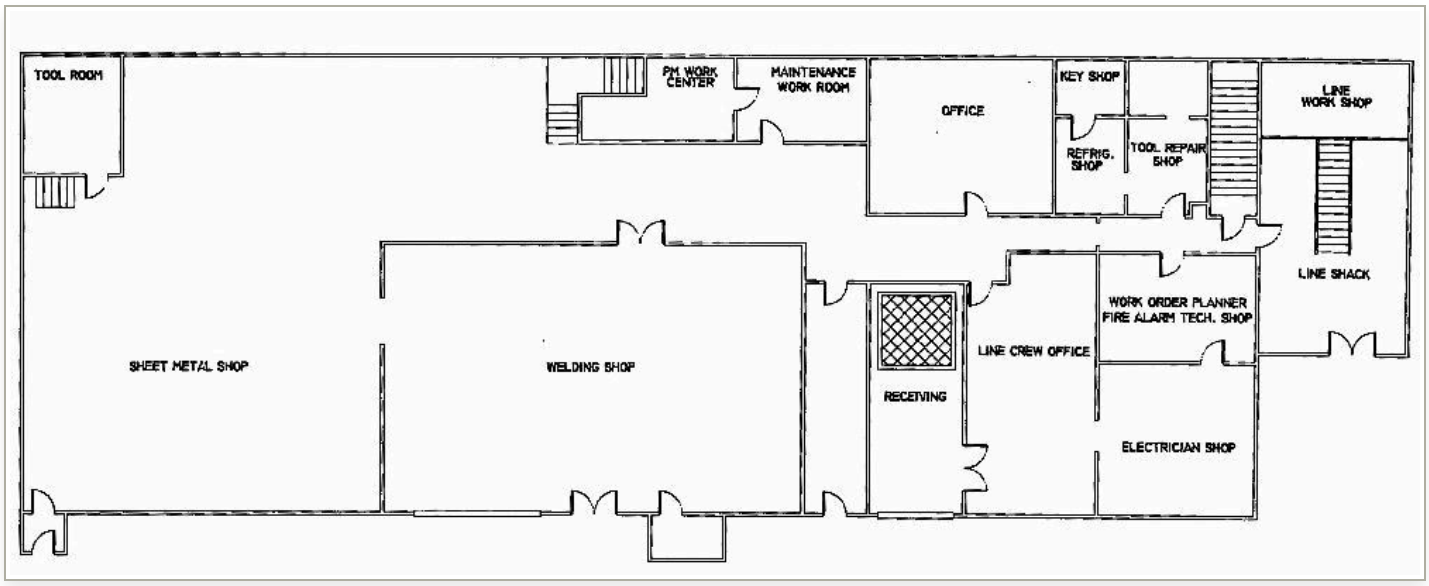


Figure 1: *Utilities - Facilities*

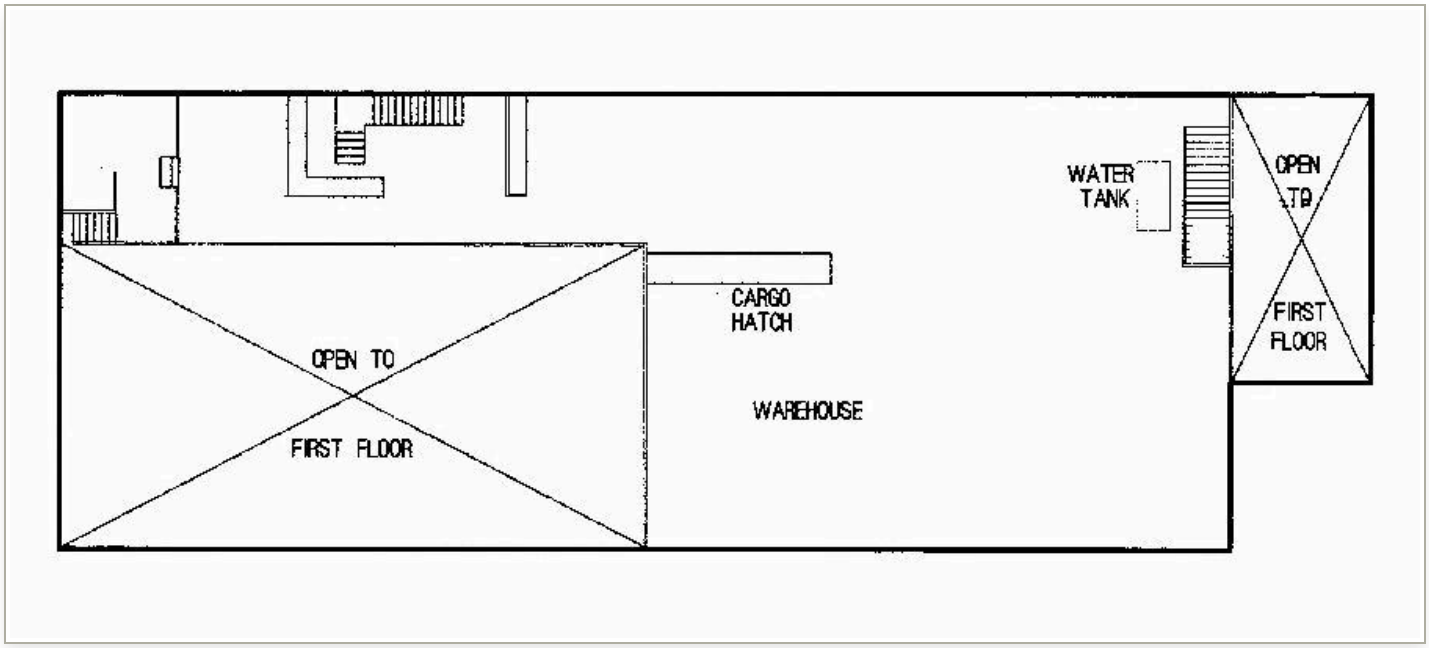


Figure 2: *Utilities - Facilities*
