McMurdo Station, Ross Island

BUILDING INFORMATION SHEET

Logistics - Materials - Mapcon; 191A - Carpentry Workshop

Location ID: B191

Two-story building used as a woodworking shop with offices on the first floor. A storage area on the second floor is used as a tool storage and issue room.

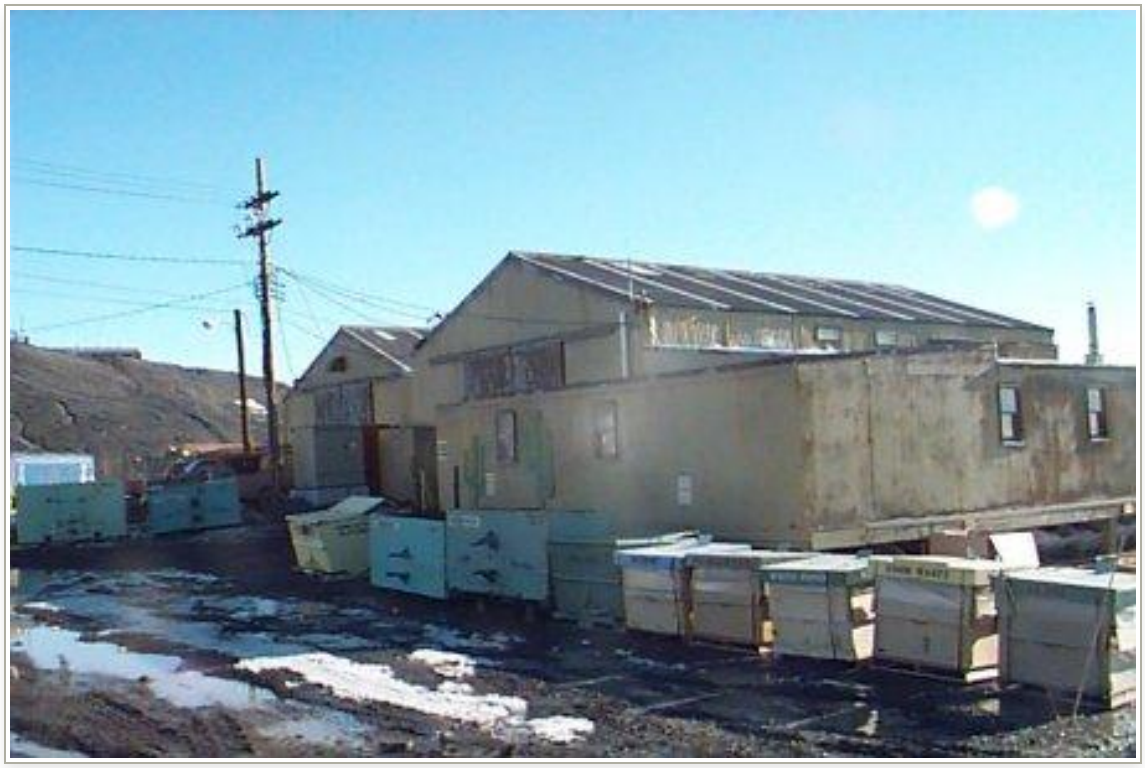


Photo 1: *Logistics - Materials - Mapcon; 191A - Carpentry Workshop*

General Structure Information



Automatic External Defibrillator (AED) Locations

This building contains one or more AED devices that may be used in the event of life-threatening cardiac arrhythmia.

- **191A, In the office on the small side of the shop**

Usage	FMC Carpentry Work Center and Tool Room (the Foldaway)
Occupancy Group	H-2 Wood shop, B-2 Office and Warehouse, and B-4 Storage
Maximum Occupancy	54
Construction Type	Type V, N, combustible; steel-framed Foldaway structure with insulated metal siding and roofing, wood-framed plywood floor, wood-framed plywood and gypsum board interior partitions.
Year Constructed	1977-78
Dimensions	44' x 54'40' x 57'35' x 52'

Floor Area

Floor	Area
Floor 1	6,476 sq ft
Floor 2	3,948 sq ft
Total	10,424 sq ft

HVAC System

Heating	Two Jackson-Church forced-air, oil-burning units (250,000 BTU/hr each)One Lennox forced-air, oil-burning unit (125,000 Btu/hr)
Air Handling Units	None
Fuel Tank	Fuel tank #1: 300 gallon, Fuel tank #2: 700 gallon

Water and Sewer

Water Service	Not connected
Sewer Service	Not connected
Connections	Sinks: 0 Toilets: 0 Urinals: 0 Showers: 0 Water Cooler: 0 7 lines with 15 instruments
Water Heater	None

Electrical Service

Service Feeder	Feeder D
Transformer	XF
Electrical Service	208/120V, 3PH, 2-225A mains in Building 1911-225A main in Building 191A
Phone and LAN	7 lines with 15 instruments

Fire System

Fire Panel Type	King-Fisher KFRTI-20 industrial radio and control system (IRACS) panel, heat detectors, pull stations, alarm horns

Floorplans

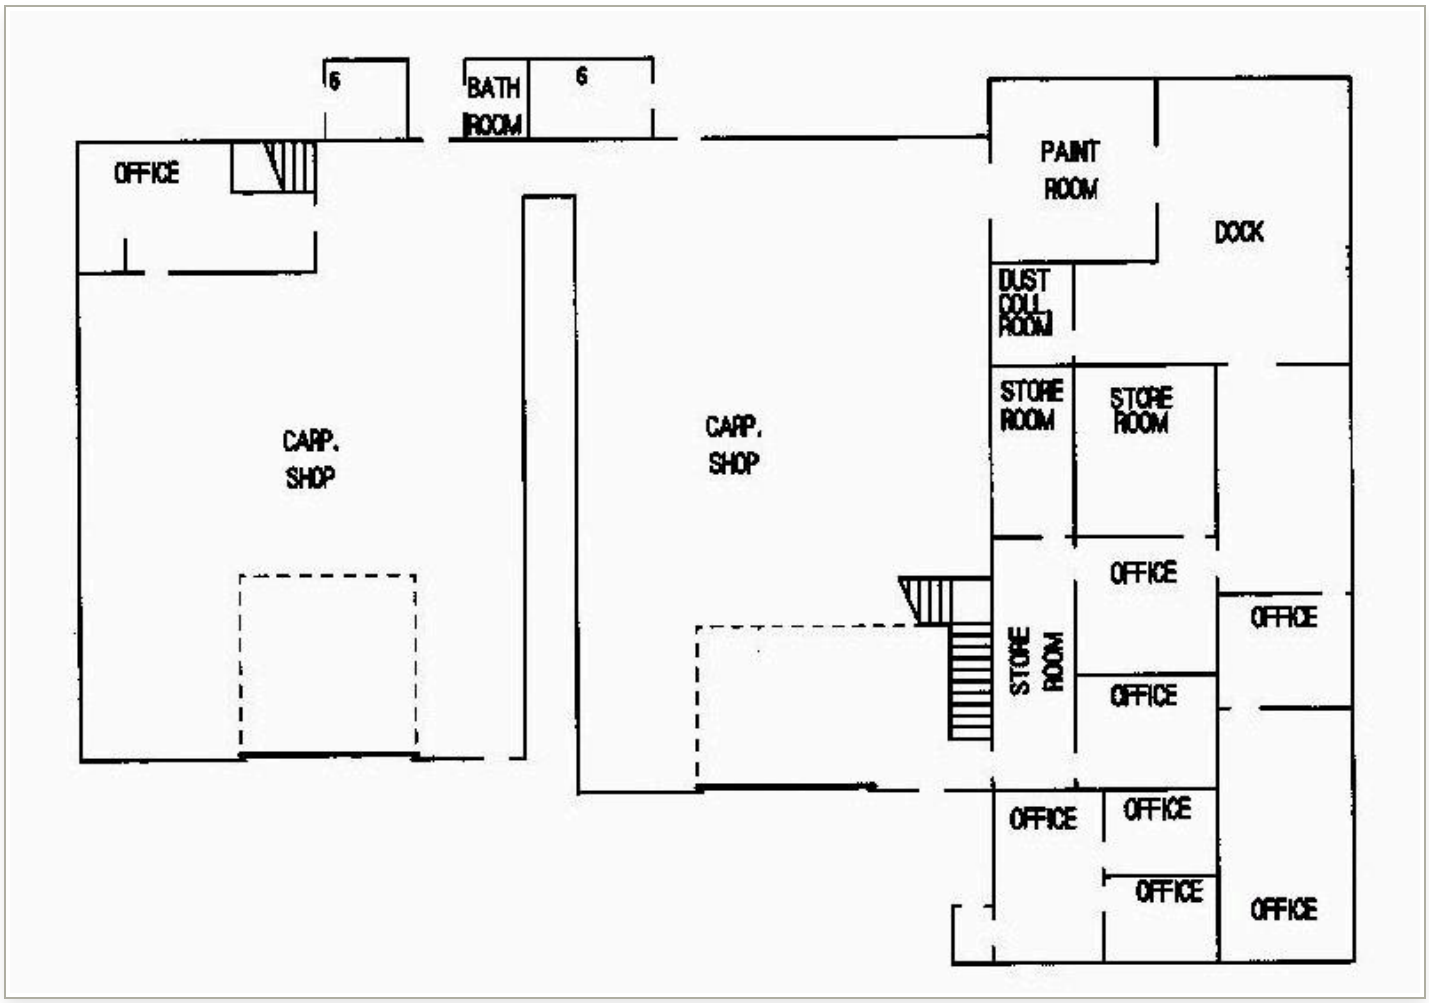


Figure 1: *Logistics - Materials - Mapcon; 191A - Carpentry Workshop*

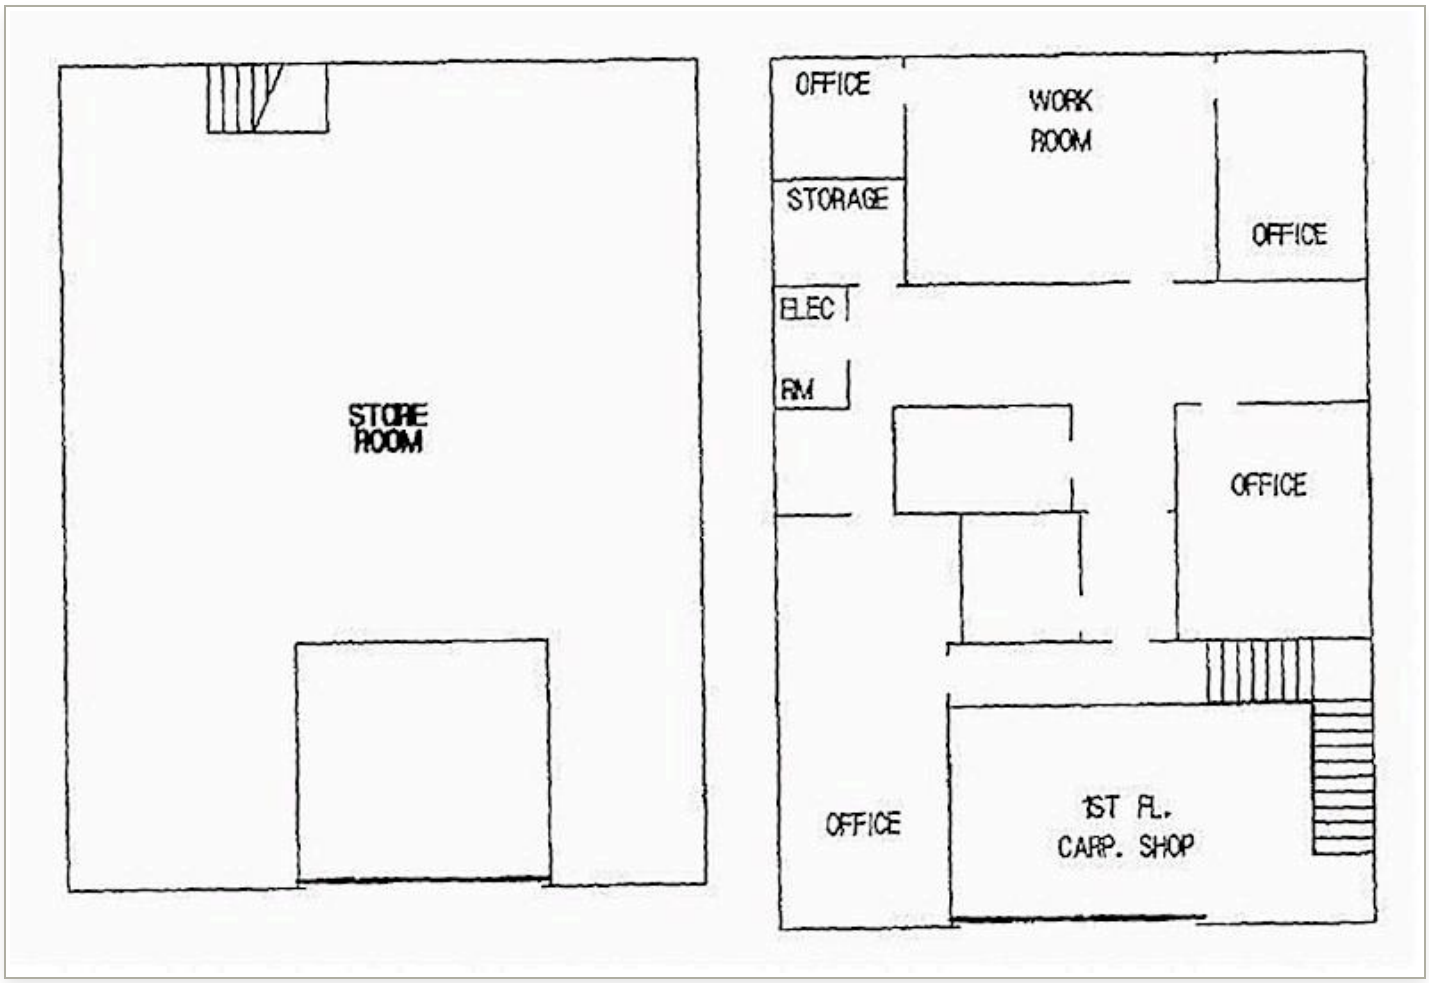


Figure 2: *Logistics - Materials - Mapcon; 191A - Carpentry Workshop*
