McMurdo Station, Ross Island

BUILDING INFORMATION SHEET

Dorm

Location ID: B208

Three-story personnel dormitory housing up to 134 persons. The first floor includes 17 two-person rooms, as well as a library, lounge, public restroom, and a sauna. The second floor includes 24 two-person rooms and a small lounge. The third floor includes 26 two-person rooms.



Photo 1: *Dorm*

General Structure Information

Usage	Dormitory
Occupancy Group	R-1 Dormitories
Maximum Occupancy	381
Construction Type	Type II, 1-Hour, non-combustible; steel-framed structure with 2-1/2" thick foam-insulated metal siding and roofing, steel-framed heavy timber first floor, steel-framed metal second and third floors. Steel-stud gypsum board interior partitions.
Year Constructed	1988-89
Dimensions	48' X 168'

Floor Area

Floor	Area
Floor 1	8,064 sq ft
Floor 2	8,064 sq ft
Floor 3	8,064 sq ft
Total	24,192 sq ft

HVAC System

Heating	York-Shipley oil-fired glycol boiler (2,009,000 Btu/hr)
Air Handling Units	Two Trane, Climate Changer air handling units. They are located at each end of the building in the attic vestibule. They supply fresh air only at 60 degrees F.
Fuel Tank	2,500 gallon tank

Water and Sewer

Water Service	2 inch
Sewer Service	4 inch
Connections	Sinks: Toilets: Urinals: 1 Showers: Water Fountains: 1 Washing Machines: 6 Ice Machine: 2 Sauna: 1 100 lines - pending verification for all buildings
Water Heater	Glycol heat exchanger with 440 gallon hot water storage tank

Electrical Service

Service Feeder	Feeder A
Electrical Service	208/120V, 3PH, 400A main
Phone and LAN	100 lines - pending verification for all buildings

Fire System

Fire Panel Type	Pyrotronics System 3 control panel, King-Fisher KFRTI-WP-8 radio interface/transmitter panel, pull stations, alarm horns
Suppression Type	Pre-action sprinkler system connected to Firetrol pump and resevoir and equipped with Star, 6-inch, model D, electromagnetic deluge valve with air pressure supervision. Deluge valve releases upon low air pressure and heat detector actuation. Firetrol pump starts on water pressure loss in main trunk line to dorms.

Floorplans

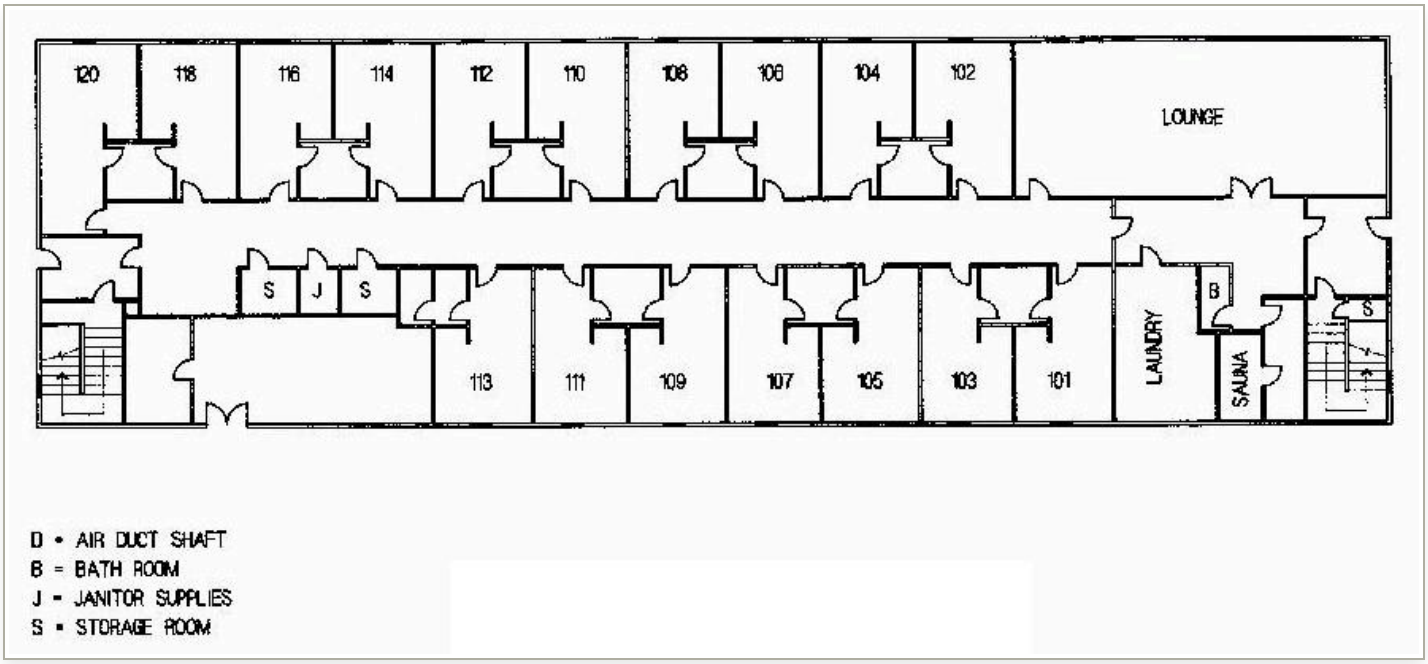


Figure 1: *Dorm*

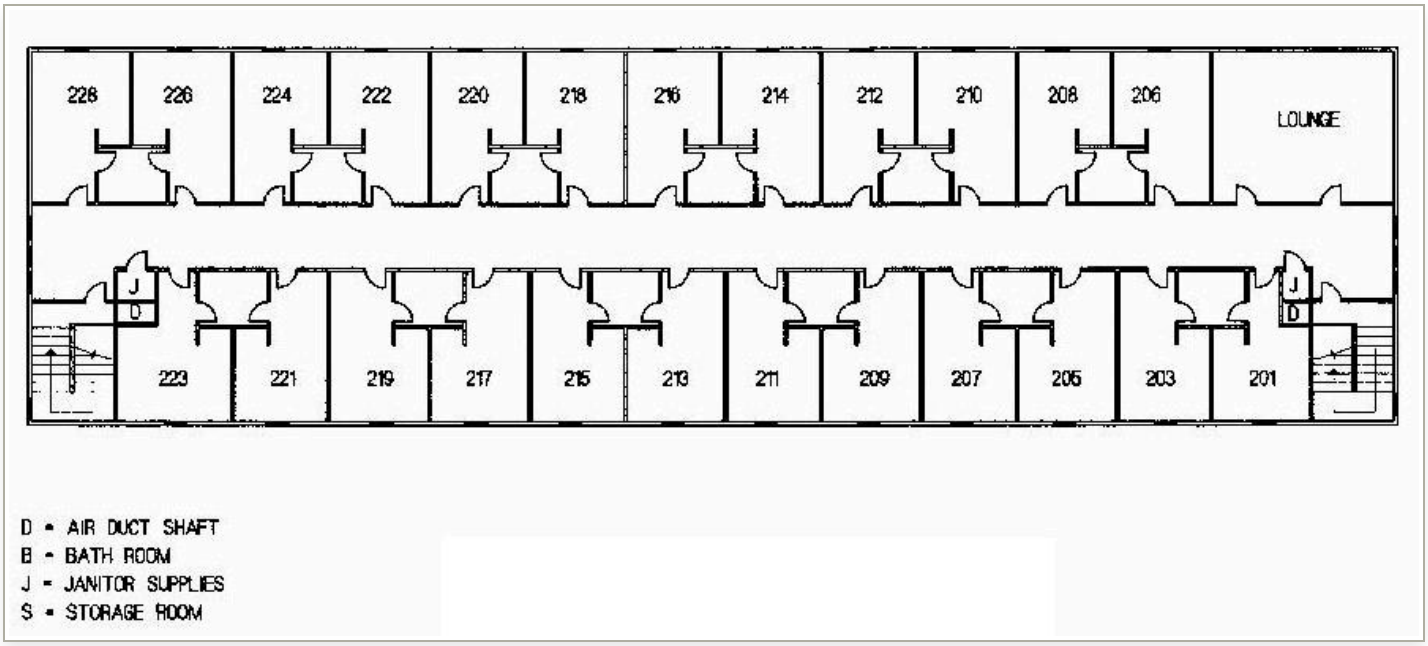


Figure 2: *Dorm*

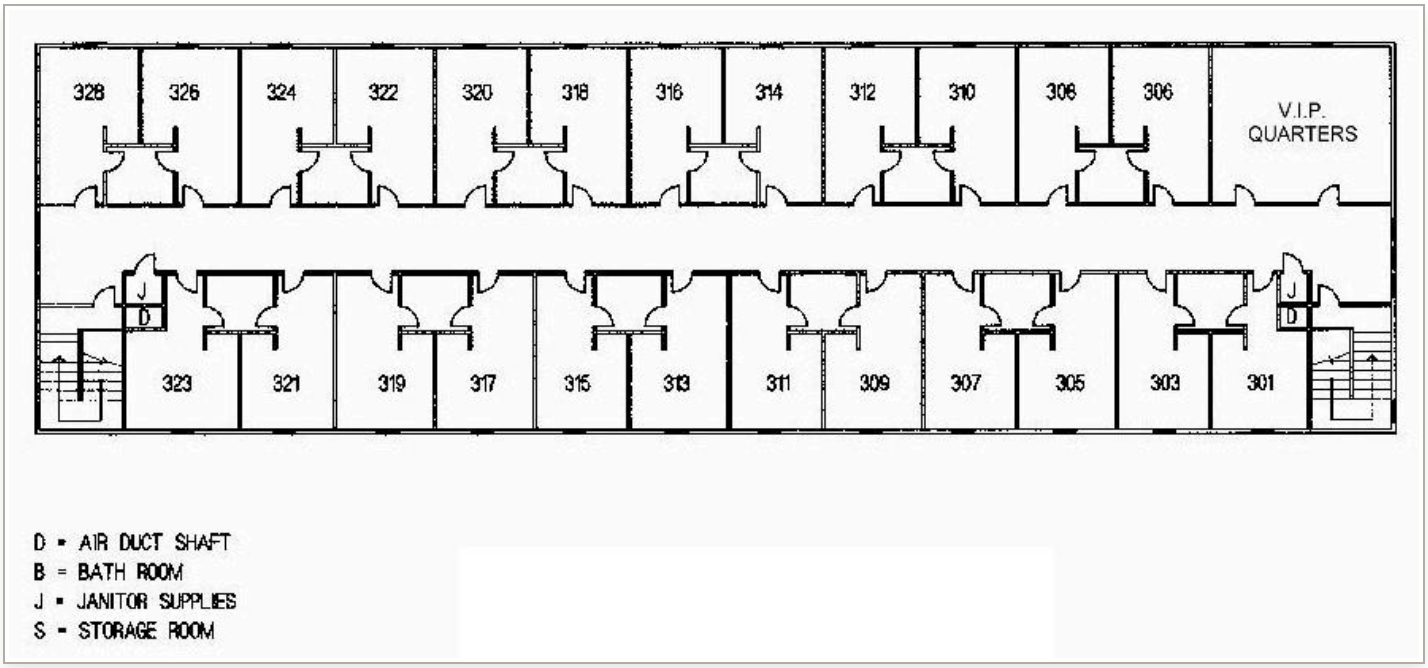


Figure 3: *Dorm*
